5:13 AM Thu 4/1/10

10 Princes' Gdns

ID		Task Name	Duration	Start	Finish	Predecessors
1		ERECT SCAFFOLD	3 days	Mon 2/15/10	Wed 2/17/10	
2		WASH FAÇADE	2 days	Thu 2/18/10	Fri 2/19/10	1
3		SIZE AND ORDER GUTTERS	2 days	Fri 2/19/10	Mon 2/22/10	2FS-1 day
4		PROVIDE LITHO SAMPLES	1 day	Mon 2/22/10	Mon 2/22/10	3FS-1 day
5		CONFIRM SURVEY	1 day	Mon 2/22/10	Mon 2/22/10	2
6		ORDER STONE	2 days	Tue 2/23/10	Wed 2/24/10	5
7		STONE DELIVERY	0 days	Wed 3/17/10	Wed 3/17/10	6FS+3 wks
8		STONE FASHIONING	4 days	Thu 3/18/10	Tue 3/23/10	7
9		INDENTS	5 days	Wed 3/24/10	Tue 3/30/10	8
10		RESURVEY STONE	1 day?	Wed 3/31/10	Wed 3/31/10	9
11		REPAIRS	5 days	Thu 4/1/10	Wed 4/14/10	10
12		MASTIC WINDOWS	2 days	Thu 4/15/10	Fri 4/16/10	11
13		MASONRY POINT	2 days	Mon 4/19/10	Tue 4/20/10	12
14		INSTAL GUTTERS/ RWP	2 days	Tue 3/23/10	Wed 3/24/10	3FS+4 wks
15		DECORATE	2 days	Wed 4/21/10	Thu 4/22/10	13
16		DISM SCAFFOLD	2 days	Fri 4/23/10	Mon 4/26/10	15
17		BOUNDARY WALL	6 days	Tue 4/27/10	Tue 5/4/10	16
18		RAILINGS & DECORATE	4 days	Wed 5/5/10	Mon 5/10/10	17

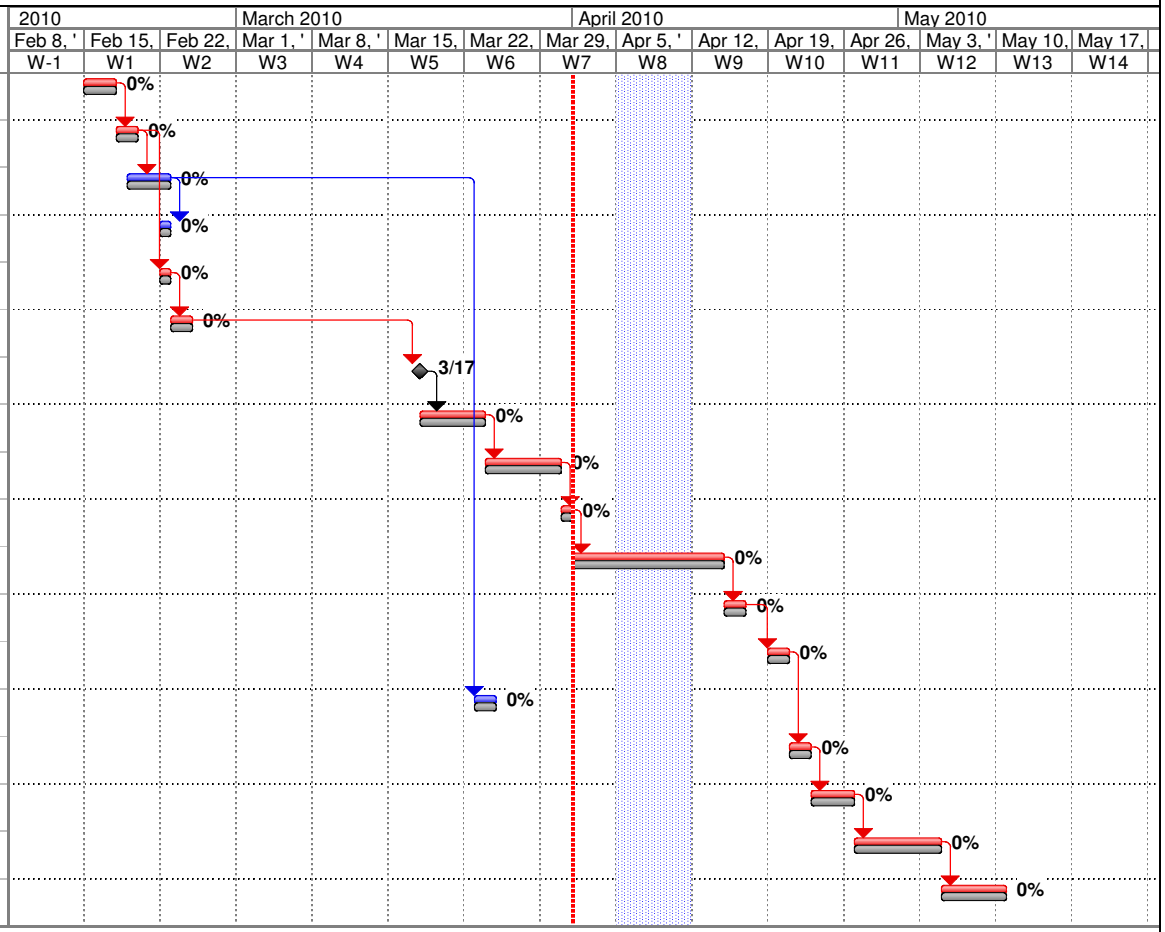

Critical		Split		Baseline Milestone		Project Summary	
Critical Split		Task Progress		Milestone		External Tasks	
Critical Progress		Baseline		Summary Progress		External Milestone	
Task		Baseline Split		Summary		Deadline	
